

# CONSTRUCTION MANAGEMENT WEEKLY PROGRESS REPORT



**2018 ROAD IMPROVEMENT PROGRAM – PHASE II**  
**West Atlantic Avenue & South Gibbs Street**  
**ERI Job # 31583 02**  
**Township of Middle**  
**County of Cape May, New Jersey**


**WEEKLY PROGRESS REPORT #8**  
**May 13, 2019 to May 17, 2019**



*Figure: 1 – Installation of concrete curb and gutter on West Atlantic Avenue along the westbound lane between South Main Street and South Boyd Street*



*Figure: 2 – Installation of concrete sidewalk on West Atlantic Avenue along the eastbound lane between South Main Street and South Boyd Street*

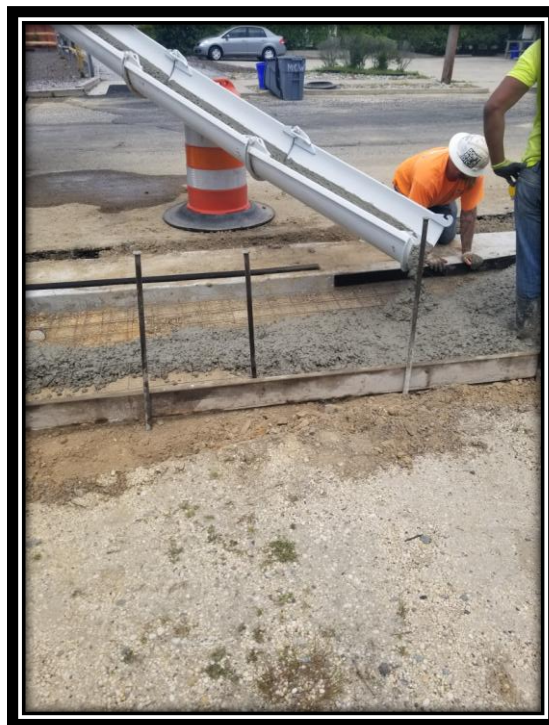

*Figure: 3 – Installation of concrete driveway apron on West Atlantic Avenue along the westbound lane between South Main Street and South Boyd Street*

**Work Completed the Week of May 13, 2019:**

South State's concrete subcontractor, Capital Concrete, mobilized to West Atlantic Avenue and began installation of the proposed concrete improvements. Capital installed 600 linear feet of concrete curb & gutter, 59.11 square yards of concrete sidewalk and 17.33 square yards of concrete driveway apron in both the eastbound and westbound lanes between South Main Street and South Boyd Street. New Jersey American Water Company was onsite to adjust the elevations of each water meter to be flush with the newly installed sidewalk.

**#6: Concrete Curb and Gutter – 600 LF**

**#7: Concrete Sidewalk, 4" Thick – 59.11 SY**

**#9: Concrete Apron, 6" Thick, Reinforced – 17.33 SY**

**Anticipated Work for the Week of May 20, 2019:**

Capital Concrete will continue concrete improvements along both lanes of West Atlantic Avenue between South Main Street and South Boyd Street. New Jersey American Water Company will continue to reset existing water meters within the proposed sidewalk to grade along West Atlantic Avenue.

**Notice to Proceed Date: March 13, 2019**

**Anticipated Completion Date: June 14, 2019**

Prepared By:



C. Jeremy Noll, PE, CME  
Project Engineer  
Environmental Resolutions, Inc.
