

# CONSTRUCTION MANAGEMENT WEEKLY PROGRESS REPORT



## 2018 ROAD IMPROVEMENT PROGRAM

Beaver Dam Road, Faith Run, Turtle Thorofare Court, Pennsylvania Avenue, South 2<sup>nd</sup> Street,  
Joffre Avenue, New Jersey Avenue, Church Street, Shell Bay Avenue, & East Main Street

ERI Job # 31583 01

Township of Middle

County of Cape May, New Jersey

## WEEKLY PROGRESS REPORT #2


April 30, 2018 to May 4, 2018



*Figure: 1 – Installation of 6” thick, reinforced concrete driveway apron on Faith Run*



*Figure: 2 – Installation of concrete curb on Church Street between North Boyd Street and North Main Street*

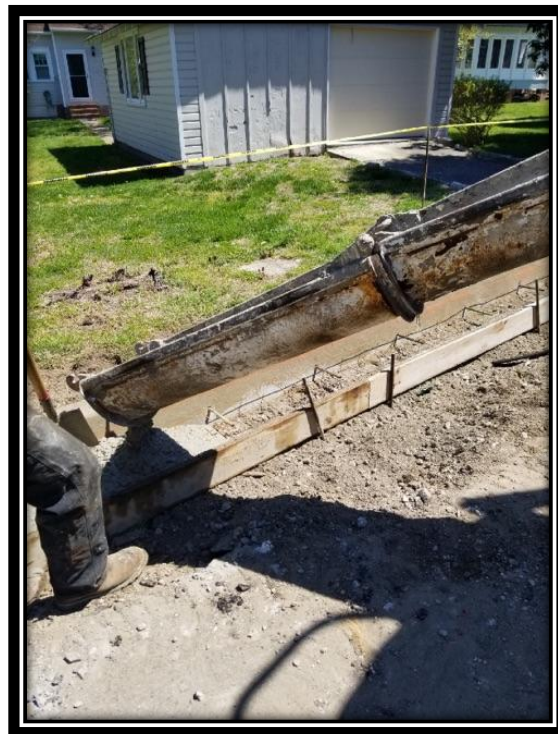

*Figure: 3 – Installation of concrete curb and gutter along Church Street between North Boyd Street and North Main Street*

**Work Completed the Week of April 30, 2018:**

Landberg Construction's concrete crew installed concrete improvements on Church Street and Faith Run. The concrete crew installed 343 linear feet of concrete curb, 14.2 square yards of concrete apron, and 311 linear feet of concrete curb and gutter. The concrete crew then completed all of the asphalt restoration in front of the newly installed concrete curb, concrete swale, and concrete curb and gutter completed to date. The crew also began topsoil and seed restoration behind the newly installed curb and sidewalk.

**#7: Concrete Curb – 343 LF**

**#10: Concrete Apron, 6" Thick, Reinforced – 14.2 SY**

**#11: Concrete Curb and Gutter – 311 LF**

**Anticipated Work for the Week of May 7, 2018:**

Landberg's concrete crew will continue concrete improvements on East Main Street. All concrete work will be completed by May 11, 2018.

**Spring Notice to Proceed Date: April 23, 2018**

**Anticipated Completion Date: June 29, 2018**

Prepared By:

A handwritten signature in blue ink that reads "C. Jeremy Noll". The signature is stylized and cursive.

C. Jeremy Noll, PE, CME  
Project Engineer  
Environmental Resolutions, Inc.
